

POTOMAC YARD METRORAIL STATION PROJECT

City Council Update
January 26, 2021

Agenda

- Project Update:
 - Southwest Access Update
 - Construction Update
 - Project Progress

Southwest Access Update

Southwest Access (DSUP Amendment)

- Grant Funds to be Awarded – February / March
- Change Order Finalized- January 7, 2021
- Site Plan Released – January 11, 2021
- Building Permit To be Issued – Late January

Southwest Access Construction Activities

- Site Preparation work underway



Construction Update



Construction Update

- Potential COVID-19 Impacts
 - PYC submittals documenting potential delays
- President's Day WMATA Outage
 - Erection of the Pedestrian Bridge span over the WMATA tracks
- Completion date - March 2022

AC Switchgear Building: Looking North



Station Mezzanine: Looking Northwest



Station Mezzanine: Floor Slab Rebar



Station Mezzanine: South Wall



East & West Platforms: Looking South



Station: East Platform Service Level



North Pavilion: Steel Erection



Knuckle Pier: Looking West from Mezzanine




Knuckle Pier:



Southwest Pavilion: Clearing



Project Progress Update

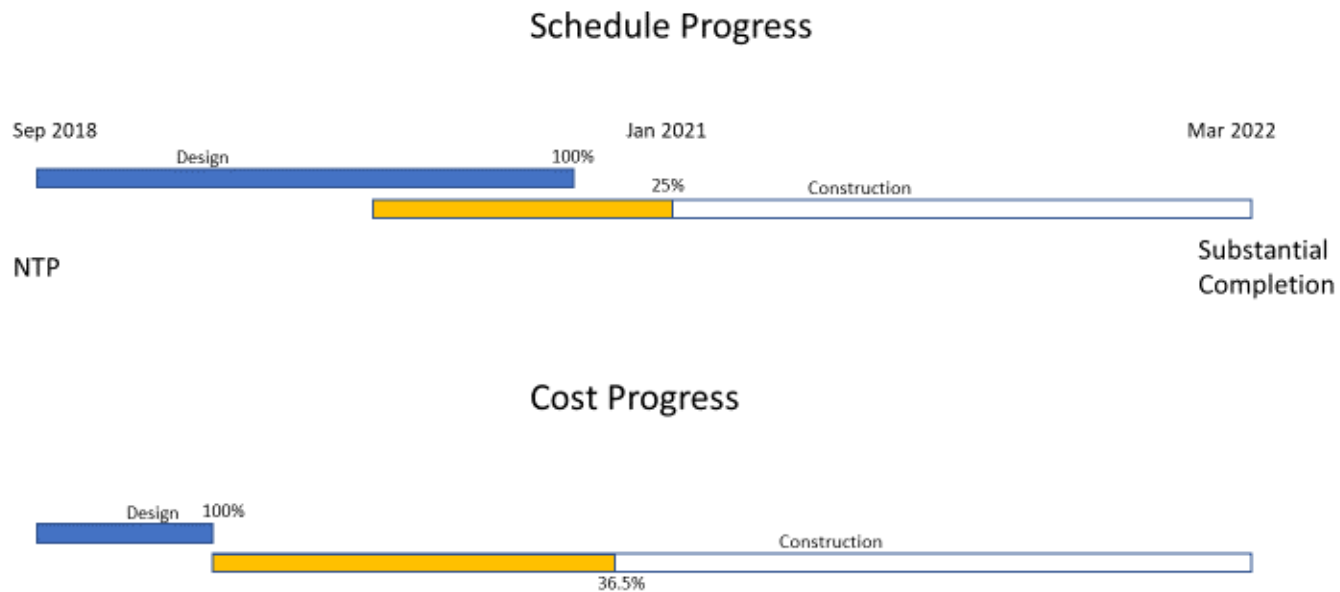

The Southwest Access is not included in these completion figures; but is planned for completion in parallel to the station construction.





Discussion

